



Technical Proposal

**Design, Development, and Operationalization
of a Modern, Interactive, & Sustainable
Organizational Website**



Proposed By:

Company Name: eTech S.C

Company Address: IT park BPO building 7th floor

Contact Person: Ahadu G/senbet

Email: Ahadu.G@etechsc.com

Phone: 0992969607

Proposed To:

Submitted to: Ethiopian Media Women
Association (EMWA)



eTech
ethical, ethiopian, end-To-end

MAY 2026

Company Background


eTech is an end-to-end ICT solutions provision company setup by highly skilled technical and business professionals from around the world. These diverse experience skills make eTech uniquely equipped to be a leading participant in the technology accelerated transformation Ethiopia has envisioned.

With a mission to create a border less ICT expertise Eco-system to do ethical end to end business anywhere, vision to be a pioneer in providing Integrated Ethical Technology Solutions in Ethiopia and noticeable player in the world by 2030 and value of Quality, Customer satisfaction, Loyalty, Trust, and Integrity, Technological excellence, and Empowering partners. Below are the pillars eTech SC stands:



ETHICAL

Maintain Business Virtue for All and Engage by Majority Acceptable Jobs Only.



ETHIOPIAN

Ethiopians' Technologies Needs Can Only Be Met by Ethiopians Foremost, Give Value, Respect and Attention for Ethiopian's Effort, Knowledge, And Innovation.



END-TO-END

Progressively Provide Entire Technology Solutions in One Table End to End.

TABLE OF CONTENTS

- 1.EXECUTIVE SUMMARY 1
- 2.INTRODUCTION..... 3
- 3. UNDERSTANDING OF THE ASSIGNMENT 4
- 4. PROJECT OBJECTIVES 6
- 5. Project Scope and Deliverables 7
 - 5.1 Project Scope 7
- 6. Proposed Technical Solution 10
- 7. FUNCTIONAL SCOPE & DELIVERABLES 16
- 8. System Architecture & Technology Stack 17
- 9. UI/UX & Accessibility Strategy 18
- 10. SEO & Digital Visibility Strategy..... 20
- 11. Security & Compliance Framework..... 20
- 12. Hosting & Infrastructure Strategy..... 21
- 13. Content Management Strategy 23
- 14. Training & Capacity Building..... 24
- 15. Project Methodology..... 25
- 16. Implementation Plan & Timeline..... 26
- 17. Team Composition 30
- 18. Quality Assurance & Testing..... 32
- 19. Risk Management Strategy 33
- 20. SUPPORT & WARRANTY 34
- 21. Mockups..... 36
- 22. Relevant Experience 38
- 23. Source Code Handover..... 43
- 24. Declarations, Confirmations & NDA..... 44

1.EXECUTIVE SUMMARY

The Ethiopian Media Women Association (EMWA) is undertaking the development of a modern, interactive, and sustainable digital platform to strengthen its role in advocacy, knowledge-sharing, and public engagement. In line with this objective, EMWA seeks to establish a centralized web-based platform that enhances visibility, accessibility, and operational efficiency across its programs and services.

eTech S.C. is pleased to submit this technical proposal for the design, development, and deployment of a comprehensive organizational website that aligns with EMWA's strategic mission and operational needs. The proposed solution delivers a fully responsive, user-friendly, and scalable web platform supported by a robust Content Management System (CMS), enabling efficient content management and long-term sustainability.

The proposed platform will incorporate all required modules, including Homepage, About Us, Updates, Membership Section, Resources Hub, Programs/Projects, Women Experts' Directory, and Contact interface. The system will be designed with a strong emphasis on accessibility, usability, structured content delivery, and inclusive design principles to ensure engagement with diverse user groups.

eTech S.C. will implement the solution using modern web technologies and best practices in UI/UX design, Search Engine Optimization (SEO), and web accessibility standards. The platform will ensure optimal performance across devices, secure system architecture, and scalability to support future growth.

In alignment with the project requirements, eTech S.C. will facilitate the identification and configuration of a reliable hosting environment while ensuring that EMWA maintains a direct contractual relationship with the hosting provider. This approach guarantees institutional ownership, transparency, and long-term operational independence.

The project will be delivered following a structured implementation approach, including requirement validation, system design, development, testing, deployment, and capacity building. Comprehensive training will be provided to empower EMWA staff with the necessary skills to manage and maintain the platform independently.

With proven experience in digital platform development, infrastructure solutions, and secure system deployment, eTech S.C. is well-positioned to deliver a high-quality, sustainable, and future-ready web platform that supports EMWA's advocacy, outreach, and knowledge-sharing objectives.

2.INTRODUCTION

eTech S.C. is pleased to present this technical proposal in response to the Ethiopian Media Women Association (EMWA) request for the design, development, and deployment of a modern, interactive, and sustainable organizational website.

The Ethiopian Media Women Association (EMWA) is a well-established organization in Ethiopia dedicated to advancing gender equality and supporting the professional development of women media practitioners. Through its advocacy initiatives, programs, and knowledge-sharing activities, EMWA plays a critical role in promoting inclusive media representation and strengthening the voice of women in the media sector.

To enhance its digital presence and improve engagement with members, partners, and the public, EMWA seeks to develop a modern and user-friendly website that serves as a central platform for communication, resource sharing, and public outreach. The platform is expected to effectively present the organization's activities, programs, resources, and expertise, while ensuring accessibility and ease of use across different user groups.

In response to these requirements, eTech S.C. proposes a comprehensive solution that includes website design, development, content structuring, CMS implementation, hosting support, and staff training. The proposed platform will be responsive, secure, and easy to manage, enabling EMWA staff to update and maintain content independently.

As a technology solutions provider with experience in developing professional and institutional websites, eTech S.C. is committed to delivering a high-quality digital platform that aligns with EMWA's mission and supports its long-term digital and organizational objectives.

3. UNDERSTANDING OF THE ASSIGNMENT

EMWA requires a modern, interactive, and sustainable website that serves as a central digital platform for advocacy, knowledge-sharing, and public outreach. The platform is expected to strengthen the organization's visibility, improve communication, and support structured engagement with members, stakeholders, and the wider public.

Beyond the stated requirements, our analysis of the Terms of Reference identifies three core strategic needs that the platform must address:

1. **Visibility and Credibility**

EMWA requires a strong digital presence that positions the organization and its members as leading professionals in the media sector. The website should highlight achievements, showcase expertise, and strengthen credibility while addressing gaps in representation.

2. **Community and Resource Hub**

The platform should act as a structured and accessible space for members to access resources, tools, and information. It should support knowledge-sharing, provide organized content, and enable ongoing engagement among members and stakeholders.

3. **Advocacy Amplification**

The website should function as a public-facing communication engine that promotes EMWA's campaigns, programs, and impact. It must effectively present updates, success stories, and key initiatives to partners, stakeholders, and donors.

In addition to these strategic pillars, the website must include key functional components such as organizational information, updates, membership engagement, resources, programs, and a women experts' directory. These components should be structured in a clear, user-friendly, and accessible layout.

The system must also include an intuitive Content Management System (CMS), enabling EMWA staff to independently manage and update content, ensuring long-term sustainability.

Furthermore, the platform should be fully responsive, accessible across different devices, and aligned with modern web usability and accessibility standards.

The requirement also highlights the need for a reliable hosting solution with a direct contractual relationship between EMWA and the hosting provider, ensuring transparency, ownership, and long-term operational independence.

Based on this understanding, eTech S.C. proposes a solution structured around these three pillars to deliver a platform that is both technically robust and strategically aligned with EMWA's mission and long-term objectives.

4. PROJECT OBJECTIVES

4.1 General Objective

The overall objective of this project is to design, develop, and deploy a modern, user-friendly, and sustainable website for the Ethiopian Media Women Association (EMWA) that enhances its digital presence and supports its mission in advocacy, knowledge-sharing, and public engagement.

4.2 Specific Objectives

The specific objectives of the project are:

1. Strengthen Visibility and Credibility

To develop a professional and engaging website that effectively showcases EMWA's mission, programs, and impact, positioning the organization and its members as leaders in promoting gender equality in the media sector.

2. Enhance Advocacy and Public Outreach

To provide a dynamic platform for publishing updates, campaigns, success stories, and institutional content, enabling EMWA to effectively communicate with stakeholders, partners, and the public.

3. Establish a Knowledge and Resource Hub

To create an organized and easily accessible repository of resources, publications, and documents that supports knowledge-sharing and capacity building.

4. Improve Member Engagement and Accessibility

To develop a structured platform that facilitates access to information, promotes interaction, and supports EMWA members through dedicated sections such as membership and experts directory.

5. Enable Efficient Content Management

To implement a user-friendly Content Management System (CMS) that allows EMWA staff to update and manage website content independently without requiring technical expertise.

6. Ensure Accessibility and User-Friendly Experience

To design a responsive and accessible website that provides a seamless user experience across devices and aligns with modern web usability and accessibility standards.

7. Deliver a Secure, Scalable, and Sustainable Platform

To ensure the website is secure, reliable, and scalable, allowing it to grow with EMWA's future needs and digital expansion.

6. Project Scope and Deliverables

5.1 Project Scope

The scope of this project covers the design, development, and deployment of a modern, interactive, and user-friendly website for the Ethiopian Media Women Association (EMWA), in line with the requirements outlined in the Terms of Reference.

The project involves the development of a fully functional digital platform that supports EMWA's core activities in advocacy, knowledge-sharing, and public engagement. The platform will be designed to provide structured access to information, promote organizational visibility, and enable efficient content management.

The scope includes the development of a responsive and accessible website that incorporates key sections such as homepage, organizational information, updates, membership, resources, programs/projects, women experts' directory, and contact interface. The system will be designed with a focus on usability, accessibility, performance, and scalability.

The project also includes the implementation of a Content Management System (CMS) to allow EMWA staff to easily manage and update content, as well as the configuration of a secure and reliable hosting environment with a direct contractual relationship between EMWA and the hosting provider.

In addition, the scope covers testing, deployment, staff training, and initial system support to ensure a smooth transition to full operational use.

5.2 Key Deliverables

The project will deliver the following key outputs:

1. Fully Functional Website Platform

A complete and responsive website aligned with EMWA's structure and requirements, accessible across desktop, tablet, and mobile devices.

2. Website Modules and Sections

Development of all required sections including:

- ✓ Homepage
- ✓ About Us
- ✓ Updates (News and Announcements)
- ✓ Membership Section
- ✓ Resources Hub
- ✓ Programs/Projects
- ✓ Women Experts' Directory
- ✓ Contact Us

3. Content Management System (CMS)

An easy-to-use CMS that enables EMWA staff to:

- Create and edit pages
- Upload and manage documents

- Publish updates and content
- Manage resources and sections independently

4. Content Structuring and Upload Support

Initial content organization, formatting, and uploading to ensure the website is operational and properly structured at launch.

5. Hosting Setup and Deployment

Configuration and deployment of the website on a secure hosting environment, with EMWA maintaining direct ownership and contractual agreement with the hosting provider.

6. Website Security and Optimization

Implementation of security measures, performance optimization, and basic SEO setup to ensure reliability and visibility.

7. Training and Knowledge Transfer

Training sessions for EMWA staff on CMS usage, content management, and basic system administration.

8. Documentation and Handover

Provision of user guidelines and documentation to support ongoing website management.

6. Proposed Technical Solution

6.1 Solution Overview

eTech S.C. proposes the development of a secure, responsive, and scalable institutional website for the Ethiopian Media Women Association (EMWA), built using modern web technologies and a robust content management framework.

The proposed platform is designed to serve as a central digital system that supports EMWA's core functions in advocacy, knowledge-sharing, and public communication.

The solution integrates the following key elements:

- Modern and responsive UI/UX design
- Enterprise-level Content Management System (CMS)
- Search Engine Optimization (SEO)
- Accessibility compliance
- Secure hosting and infrastructure
- Structured content management workflows
- Modular and scalable architecture
- Centralized administrative control

This integrated approach ensures that EMWA benefits from a high-performance, secure, and sustainable platform aligned with its operational and strategic needs.

6.2 Core Solution Components

Responsive Institutional Website

The platform will be developed as a fully responsive website optimized for:

- Desktop devices
- Tablets
- Mobile phones
- Modern web browsers

This ensures consistent performance and usability across all user environments.

Enterprise Content Management System (CMS)

The proposed solution will incorporate a secure, user-friendly, and scalable Enterprise Content Management System (CMS) that enables EMWA to efficiently manage and control all website content without requiring advanced technical expertise.

The CMS will serve as the core administrative engine of the platform, providing structured tools for content creation, organization, publication, and management across all website modules.

Key Capabilities

The CMS will enable EMWA staff to:

- Create, edit, and publish web pages and content sections
- Manage news, updates, and announcements
- Upload and organize documents, publications, and media files
- Maintain structured data such as the Women Experts' Directory
- Manage programs, projects, and resource content
- Control user roles, permissions, and access levels

User Roles and Access Control

The system will include role-based access management to ensure secure and organized operation:

- **Administrators:** Full system control, including content publishing and user management
- **Editors:** Ability to create and manage content
- **Contributors (optional):** Content submission with controlled publishing rights

This ensures proper governance, accountability, and structured content management.

Content Workflow Management

To support quality control and consistency, the CMS will allow:

- Drafting and reviewing content before publication
- Scheduled publishing of updates and announcements
- Editing and updating existing content
- Structured organization of website sections

Usability and Sustainability

The CMS will be designed with simplicity and usability as a priority, ensuring that:

- EMWA staff can manage content independently
- Minimal technical support is required for routine updates
- The platform remains sustainable for long-term use

Resource & Knowledge Hub

The Resource and Knowledge Hub will be developed as a centralized digital repository designed to store, organize, and provide easy access to EMWA's knowledge assets, publications, and advocacy materials.

This module will serve as a key component in supporting knowledge-sharing, capacity building, and public access to information.

Core Features

The hub will provide structured access to a wide range of content, including:

- Reports and publications
- Research documents and policy briefs
- Advocacy materials and campaigns
- Media resources and communication materials
- Training manuals and reference documents

All resources will be organized in a clear and structured format for easy navigation and usability.

Content Organization and Access

The system will ensure efficient organization and retrieval of resources through:

- Categorization by topic, program, or content type
- Search functionality for quick access to documents
- Structured listing of resources with descriptions and metadata
- Download and viewing capabilities for multiple file formats

This ensures that users can easily locate relevant information with minimal effort.

User Access and Management

The Resource Hub will support controlled content management by EMWA administrators:

- Uploading and updating documents
- Organizing and categorizing resources
- Editing and maintaining content over time
- Managing visibility of sensitive or public materials

This ensures that the hub remains accurate, updated, and aligned with EMWA's communication needs.

Strategic Value

The Resource and Knowledge Hub will:

- Support knowledge-sharing across EMWA programs
- Improve accessibility of institutional resources
- Enhance transparency and information dissemination
- Provide a reliable reference platform for stakeholders, researchers, and the public

Membership & Engagement Module

The Membership and Engagement Module will be designed to support interaction between EMWA, its members, and external stakeholders. This component will provide structured access to membership information and facilitate communication and engagement through the website.

Core Features

The module will include:

- Membership information pages outlining benefits, categories, and requirements
- Online inquiry and application forms
- Contact and communication forms for stakeholders
- Structured presentation of membership-related content

User Interaction

The system will enable:

- Prospective members to access information and submit inquiries
- Stakeholders and partners to communicate with EMWA through web forms
- Easy access to relevant membership resources and updates

Content Management

EMWA administrators will be able to:

- Manage membership-related content
- Update information on joining procedures and requirements
- Monitor and respond to inquiries submitted through the website
- Maintain structured engagement content

Programs & Projects Module

A dedicated section to showcase EMWA's programs, projects, and initiatives.

Key Features

- Display ongoing and completed programs
- Highlight campaigns and advocacy activities
- Present impact stories and key results
- Include project documents, images, and media
- Show donor and partner information

SEO & Analytics Integration

The platform will include essential SEO and analytics features to improve visibility and performance.

Key Features

- On-page SEO optimization (meta titles, descriptions, clean URLs)
- Image optimization with alt tags

- XML sitemap for search engine indexing
- Integration with analytics tools (e.g., website traffic monitoring)

Purpose

- Improve search engine visibility
- Enable performance tracking and reporting
- Support data-driven decision making

Security & Backup Framework

The platform will include essential security and backup mechanisms to ensure data protection, system reliability, and continuous availability.

Key Features

- SSL encryption (HTTPS secure access)
- Role-based user access control
- Firewall and basic threat protection
- Automated backups and recovery setup
- Protection against common web vulnerabilities

Purpose

- Ensure platform security and data integrity
- Prevent unauthorized access and system risks
- Enable fast recovery in case of data loss or failure

7. FUNCTIONAL SCOPE & DELIVERABLES

7.1 Website Structure

The proposed website will include the following structured sections:

1. Homepage

- ✓ Institutional overview
- ✓ Hero banners and highlights
- ✓ Featured updates and announcements
- ✓ Quick access navigation
- ✓ Highlighted resources and projects

2. About Us

- ✓ Organization history
- ✓ Vision, mission, and objectives
- ✓ Governance structure
- ✓ Leadership profiles
- ✓ Organizational values

3. Programs & Projects

- ✓ Program and project listings
- ✓ Detailed project descriptions
- ✓ Outcomes and impact highlights
- ✓ Donor and partner information
- ✓ Media attachments

4. Updates & News

- ✓ News and announcements publishing
- ✓ Press releases and media updates
- ✓ Events and activities
- ✓ Archived updates

4. Membership Section

- ✓ Membership information
- ✓ Inquiry and registration forms
- ✓ Member-related resources
- ✓ Engagement opportunities

5. Women Experts' Directory

- ✓ Searchable expert directory
- ✓ Categorized expertise areas
- ✓ Individual professional profiles
- ✓ Contact request functionality

6. Resources Hub

- ✓ Downloadable publications
- ✓ Reports and research documents
- ✓ Media and communication materials
- ✓ Knowledge-sharing resources

7. Contact Us

- ✓ Contact and inquiry forms
- ✓ Office and location details
- ✓ Map integration
- ✓ Communication channels

8. System Architecture & Technology Stack

8.1 Frontend Technologies

The user interface will be developed using modern web technologies to ensure responsiveness, usability, and accessibility:

- **HTML5** and **CSS3** for structured and styled content
- **JavaScript** for dynamic interactions
- **Bootstrap** or **Tailwind** framework for responsive layout
- Mobile-first responsive UI architecture

8.2 Backend Technologies

The backend system will be built using a scalable and maintainable architecture:

- PHP (with Laravel framework where applicable)
- CMS integration for content management (WordPress-based/optional)
- RESTful architecture for structured data handling
- Modular administration for flexibility and scalability

8.3 Database

The system will utilize a reliable relational database for structured data storage:

- MySQL or MariaDB
- Secure and optimized data management
- Support for scalable content and user data

8.4 Hosting Environment

The platform will be deployed in a secure and stable hosting environment:

- Linux-based hosting infrastructure
- SSL-enabled secure access (HTTPS)
- Backup-enabled system configuration

8.5 Third-Party Integrations

The system will integrate with standard tools to enhance functionality:

- Google Analytics for traffic monitoring
- SEO tools for search optimization
- SMTP email integration for communication forms
- Social media integration
- Google Search Console for indexing and performance tracking

8.6 Scalability Considerations

The system architecture will be designed to support future growth and expansion, including:

- Addition of new modules and features
- Integration with external systems via APIs
- Multi-language support
- Handling increasing user traffic
- Expansion of content and resource repositories

9. UI/UX & Accessibility Strategy

9.1 Design Philosophy

The user interface will be designed based on the following principles:

- Simplicity and clarity
- Accessibility and inclusivity
- Professional and institutional design
- Consistent branding
- User-centered navigation
- Fast and easy information access

9.2 UX Objectives

The design approach aims to:

- Improve user engagement
- Simplify navigation and content access
- Enhance overall usability
- Optimize experience for mobile users
- Improve readability of content

9.3 Accessibility Standards

The platform will follow accessibility best practices to ensure inclusive use:

- WCAG-aligned accessibility standards
- Clear and readable typography
- Accessible color schemes and contrast
- Keyboard navigation support
- Mobile accessibility optimization

9.4 Mobile Responsiveness

The platform will be fully responsive and optimized for:

- Smartphones
- Tablets
- Laptops
- Desktop systems

10. SEO & Digital Visibility Strategy

10.1 SEO Objectives

To enhance EMWA's online visibility, improve search engine ranking, and expand digital reach to stakeholders, partners, and the public.

10.2 SEO Deliverables

The platform will incorporate:

- SEO-friendly URL structures
- Metadata optimization (titles and descriptions)
- Structured content hierarchy (headings)
- Search engine indexing setup
- Website performance optimization
- XML sitemap generation
- Mobile SEO optimization
- Image optimization (alt tags, sizes)
- Keyword-oriented content structure

10.3 Analytics & Monitoring

The system will integrate tools for performance tracking and insights, including:

- Google Analytics for traffic analysis
- Search Console for indexing and performance monitoring
- Website performance monitoring tools
- Visitor behavior and engagement tracking

11. Security & Compliance Framework

11.1 Security Objectives

The proposed platform will be designed to ensure the protection of EMWA's organizational data, maintain system integrity, and secure all user interactions across the website.

11.2 Security Approach

eTech S.C. will implement a layered security approach covering infrastructure, application, and operational levels to ensure a secure and reliable system.

At the infrastructure level, the platform will operate within a secure hosting environment configured with SSL encryption to ensure protected data transmission. The system will be supported by appropriate firewall configurations and secure server setup to mitigate external threats.

At the application level, the website will incorporate controlled access mechanisms, including role-based user permissions and secure authentication processes. The CMS will be configured following security best practices, including input validation and protection against common vulnerabilities. To ensure data reliability, an automated backup mechanism will be implemented, supported by defined recovery procedures. This will allow restoration of the system in case of data loss or system failure.

In addition, continuous monitoring and maintenance practices will be applied, including system updates, basic security monitoring, and vulnerability management to ensure the platform remains secure over time.

11.3 Expected Outcome

This framework ensures:

- Protection of sensitive data and system integrity
- Reliable system availability and recovery capability
- Secure and controlled access to administrative functions

12. Hosting & Infrastructure Strategy

12.1 Hosting Approach

eTech S.C. proposes a secure, reliable, and scalable hosting strategy that ensures optimal performance, system availability, and long-term sustainability of the EMWA platform.

In alignment with the Terms of Reference, the hosting model will be structured to ensure that EMWA retains full ownership and direct contractual control over the hosting environment, while eTech S.C. provides technical guidance, configuration, and deployment support.

12.2 Infrastructure Design

The platform will be deployed on a secure Linux-based hosting infrastructure configured to support performance, security, and scalability requirements. The environment will be optimized for web application hosting and structured to ensure consistent uptime and system reliability.

The hosting configuration will include essential components such as secure HTTPS access (SSL-enabled), optimized server resources, and automated backup mechanisms to ensure data protection and continuity.

12.3 Performance and Reliability

The infrastructure will be configured to provide stable and efficient system performance across all user interactions. This includes optimized server configuration, efficient content delivery, and resource management to support varying traffic levels.

Backup and recovery mechanisms will be implemented to ensure system availability and protect against data loss, supporting continuous operation of the platform.

12.4 Security Integration

The hosting environment will be integrated with core security measures, including secure communication protocols, controlled access configurations, and protection against common web-based threats. This ensures that both data and system operations remain protected at all times.

12.5 Scalability and Future Growth

The infrastructure will be designed with scalability in mind, allowing EMWA to expand the platform as needed. This includes the ability to accommodate increased traffic, additional content, and future system enhancements without requiring major reconfiguration.

13. Content Management Strategy

13.1 CMS Objectives

The Content Management System (CMS) is designed to enable EMWA staff to independently manage, update, and control all website content efficiently, ensuring long-term sustainability and minimal reliance on technical support.

13.2 CMS Capabilities

The platform will include a user-friendly administrative interface that simplifies content operations across all website sections.

It will support structured content management, including page creation, media handling, publication management, and organized categorization of content. Built-in workflow functionality will allow content to move through draft, review, and publishing stages, ensuring quality and consistency.

In addition, the system will include integrated tools to support search optimization, enabling EMWA to maintain well-structured and discoverable digital content.

13.3 Administrative Roles and Access Control

The CMS will implement a role-based access model to ensure controlled and secure content management:

- **Super Administrator:** Full system control, including user management and platform configuration
- **Content Administrator:** Responsible for managing and publishing content across the platform
- **Editor:** Reviews and refines content prior to publication
- **Contributor:** Creates and submits draft content for approval

14. Training & Capacity Building

14.1 Objective

The objective of this component is to ensure that EMWA staff are fully equipped to manage, operate, and maintain the website independently, enabling long-term sustainability and effective use of the platform.

14.2 Training Approach

eTech S.C. will deliver structured training sessions tailored to the needs of EMWA staff, focusing on both practical usage and basic system understanding.

The training will cover key areas such as content creation and management, updating website sections, uploading publications, and managing resources through the CMS. Staff will also be guided on how to handle routine administrative tasks, including managing updates and maintaining content consistency.

The approach will be hands-on and practical, ensuring participants gain direct experience using the system in real scenarios.

14.3 Capacity Building

Beyond initial training, the engagement will include knowledge transfer to ensure EMWA builds internal capacity to sustain the platform over time.

Supporting materials, including user guidelines and reference documents, will be provided to assist staff in ongoing system use and management. This ensures that knowledge is retained within the organization and can be shared internally as needed.

14.4 Outcome

This approach ensures that EMWA:

- Has full operational control of the platform
- Can independently manage and update content
- Reduces reliance on external technical support
- Maintains long-term sustainability of the system

15. Project Methodology

15.1 Approach

eTech S.C. will adopt a structured and collaborative project methodology designed to ensure timely delivery, quality assurance, and full alignment with EMWA's requirements.

The approach follows a phased implementation model, enabling continuous validation, stakeholder engagement, and controlled execution throughout the project lifecycle.

15.2 Implementation Phases

The project will be executed through the following phases:

Phase 1: Inception & Requirement Validation

Project kickoff, stakeholder engagement, and confirmation of functional and technical requirements. This phase ensures clear alignment on scope, expectations, and deliverables.

Phase 2: Design & Planning

Development of the website structure, information architecture, and UI/UX design, aligned with EMWA's branding and usability requirements.

Phase 3: Development & Configuration

Implementation of the website, CMS setup, and configuration of all modules, including content structures, directories, and resource management components.

Phase 4: Testing & Quality Assurance

Comprehensive testing of all system components, including functionality, usability, performance, and compatibility across devices and browsers.

Phase 5: Deployment & Go-Live

Deployment of the system to the hosting environment, final system validation, and preparation for live operation.

Phase 6: Training & Handover

Training of EMWA staff, system handover, and knowledge transfer to ensure independent operation and content management.

15.3 Quality Assurance

Quality control will be maintained throughout all phases of the project to ensure that deliverables meet defined standards. Each phase will include validation, issue resolution, and alignment with agreed requirements.

15.4 Client Engagement

The implementation process will include continuous coordination with EMWA through regular updates, feedback sessions, and milestone approvals, ensuring transparency and alignment at all stages.

16. Implementation Plan & Timeline

16.1 Project Delivery Approach

eTech S.C. will implement the EMWA website using an **Agile, sprint-based delivery methodology** designed to ensure rapid development, continuous stakeholder engagement, and strict adherence to the defined project timeline.

Unlike traditional delivery approaches, this methodology enables EMWA stakeholders to actively participate throughout the project lifecycle through structured sprint reviews, milestone validations, and demonstration sessions.

This ensures early feedback, fast issue resolution, and continuous alignment with EMWA's expectations.

The approach supports:

- Continuous progress tracking and transparency
- Early identification and resolution of issues

- Structured quality control at every stage
- Timely and controlled project delivery

16.2 Official Project Timeline

The implementation will follow the agreed schedule:

Project Start Date:	May 25, 2026
Project Completion & Go-Live:	June 20, 2026
Total Duration:	19 Working Days

16.3 Phase-Based Implementation Plan

The project will be executed in four structured phases:

Week 1: Discovery, Planning & Design (May 25 – May 29)

This phase focuses on project initiation, requirement validation, and design preparation.

Key activities include stakeholder workshops, user journey mapping, information architecture development, and UI/UX design creation. Wireframes and homepage concepts will be developed and refined through feedback sessions.

Key Deliverables:

Approved sitemap, validated wireframes, UI/UX design approval, and finalized technical approach.

Week 2: Core Platform Development (June 1 – June 5)

This phase focuses on establishing the foundation of the system. Core website components and CMS configuration will be implemented, including primary pages such as Home, About, Updates, and Contact.

Key Deliverables:

Functional homepage, CMS environment setup, core navigation structure, and responsive layout.

Week 3: Advanced Features & Integration (June 8 – June 12)

During this phase, advanced modules such as Membership, Women Experts' Directory, Programs & Projects, and Resource Hub will be developed and integrated. SEO, accessibility, and system optimization activities will also be applied.

Key Deliverables:

Operational directory module, search functionality, optimized content structure, and accessibility compliance.

Week 4: Testing, Training & Go-Live (June 15 – June 20)

The final phase focuses on validation, refinement, and deployment. The platform will undergo full testing, including functional, performance, and user acceptance testing (UAT). Training sessions will be delivered, followed by final deployment and launch.

Key Deliverables:

Fully tested system, trained EMWA staff, configured backup system, and live website deployment.

16.4 Detailed Work Plan

A detailed implementation schedule will guide execution across all phases, covering activities such as requirement validation, design, development, content migration, testing, training, and deployment.

Responsibilities will be assigned across project teams including project management, UI/UX, development, QA, and training to ensure accountability and coordinated delivery throughout the project timeline.

16.5 Delivery Commitment

eTech S.C. formally commits to delivering the EMWA website platform within the defined timeline of **May 25 – June 20, 2026**.

The implementation plan has been carefully structured to ensure:

- Timely and efficient delivery
- Continuous stakeholder engagement
- Controlled quality assurance
- Smooth transition to live operation
- Long-term sustainability and usability

16.7 Detailed Work Plan

The table below presents the complete implementation schedule with clearly defined activities, responsibilities, and timelines.

Task ID	Activity	Lead	Start Date	End Date	Duration
1.0	Project Inception & Requirement Gathering	Project Manager	May 25	May 26	2 Days
1.1	Kick-off Meeting with EMWA Stakeholders	Project Team	May 25	May 25	1 Day
1.2	UX/UI Workshop & Wireframe Planning	UI/UX Lead	May 25	May 26	2 Days
2.0	UI/UX Design & Approval	UI/UX Team	May 27	May 29	3 Days
2.1	Homepage & Layout Mockups	Design Team	May 27	May 28	2 Days
2.2	Design Validation & Sign-off	EMWA & eTech	May 29	May 29	1 Day
3.0	Core Website Development	Development Team	June 1	June 12	10 Days



3.1	Homepage, About & Contact Development	Frontend Team	June 1	June 3	2 Days
3.2	CMS Configuration & User Roles	Backend Team	June 2	June 4	3 Days
3.3	Membership & Experts Directory Development	Senior Developers	June 5	June 10	4 Days
3.4	Content Migration & Upload	Content Team	June 5	June 12	6 Days
3.5	SEO & Accessibility Optimization	SEO Specialist	June 10	June 12	3 Days
4.0	Testing & Quality Assurance	QA Team	June 12	June 16	3 Days
4.1	Functional & Security Testing	QA & Security Team	June 12	June 14	2 Days
4.2	User Acceptance Testing (UAT)	EMWA & eTech	June 15	June 16	2 Days
5.0	Training, Launch & Handover	Project Manager	June 17	June 20	4 Days
5.1	CMS & Website Administration Training	Training Team	June 18	June 18	1 Day
5.2	Final Security & Backup Configuration	Security Team	June 19	June 19	1 Day
5.3	Production Deployment & Go-Live	Project Team	June 20	June 20	1 Day

17. Team Composition

17.1 Overview

eTech S.C. will assign a dedicated and multidisciplinary project team to ensure the successful delivery of the EMWA website. The team structure covers all critical areas of the project including project management, system design, development, security, quality assurance, content management, and training.

Each role is clearly defined to ensure accountability, efficient coordination, and high-quality delivery across all implementation phases.

17.2 Proposed Project Team

Role	Name	Key Responsibilities	Experience / Expertise
Project Manager	Million Yitbarek	Overall coordination, stakeholder communication, timeline and delivery management	Project leadership and delivery oversight
Technical Lead / Solution Architect	Endashaw Aweke	System architecture design, technical strategy, and integration oversight	System design, CMS architecture, and scalability
UI/UX Designer	Kalkidan Getenet	User interface design, user experience optimization, and design consistency	UI/UX design and usability principles
Web Developer (Full Stack)	Meseret	Frontend and backend development, CMS implementation	HTML, CSS, JavaScript, modern frameworks, CMS development
Security & System Support	Makda Mihret	Security configuration, vulnerability mitigation, and system protection	Security assessment and compliance
QA & Testing Specialist	Ayana Ferede	Functional testing, validation, and system quality assurance	QA processes and testing methodologies
Content & SEO Specialist	Tewodros Mulie	Content structuring, SEO optimization, and content migration	SEO strategy and digital content management

17.3 Team Structure and Coordination

The project team will operate under a structured coordination model led by the Project Manager, who will serve as the primary liaison with EMWA.

The team will follow a collaborative workflow aligned with the implementation methodology, ensuring:

- Continuous stakeholder engagement
- Clear communication across all phases
- Coordinated execution between design, development, and testing teams
- Timely delivery of milestones and outputs

17.4 Resource Commitment

eTech S.C. commits to assigning qualified and dedicated personnel to this project for its full duration. Each team member will contribute according to their area of expertise, ensuring efficient resource utilization and successful project delivery.

17.5 Supporting Documentation

Detailed CVs and professional profiles of key personnel will be provided in the annex section of this proposal.

18. Quality Assurance & Testing

18.1 QA Objectives

The objective of this component is to ensure that the EMWA website is delivered as a stable, secure, reliable, and high-performing platform aligned with all functional and technical requirements.

18.2 Testing Strategy

eTech S.C. will apply a structured quality assurance approach covering all critical areas of system validation throughout the project lifecycle.

Testing activities will include validation of system functionality, usability, performance, and security to ensure the platform operates efficiently across different environments and user scenarios.

18.3 Key Testing Areas

The quality assurance process will focus on the following:

- **Functional Testing:** Verification of all website modules, content workflows, and system functionalities
- **Responsive Testing:** Validation across devices and browsers to ensure consistent user experience
- **Security Testing:** Verification of security measures and protection against common vulnerabilities
- **Performance Testing:** Optimization of loading speed and system responsiveness
- **User Acceptance Testing (UAT):** Final validation with EMWA stakeholders to ensure alignment with expectations

19. Risk Management Strategy

19.1 Overview

eTech S.C. will adopt a proactive risk management approach to identify, assess, and mitigate potential risks that may impact project delivery, timelines, or quality.

The strategy focuses on early identification and structured mitigation planning to ensure smooth project execution.

19.2 Risk Identification and Mitigation

Risk	Mitigation Strategy
Content delays	Early coordination with EMWA and structured content submission schedule
Hosting delays	Early engagement and pre-configuration of hosting environment
Scope expansion	Controlled change management and formal approval process
Security vulnerabilities	Implementation of security best practices, testing, and hardening
User adoption challenges	Comprehensive training and knowledge transfer

20. SUPPORT & WARRANTY

20.1 Warranty Period

eTech S.C. shall provide a minimum one (1) year warranty commencing from the date of formal system commissioning and acceptance.

Warranty Coverage Includes:

- Correction of system defects or errors
- Bug fixes related to delivered functionalities
- Resolution of system stability and performance issues
- Support for issues arising from normal system usage

Warranty services will be provided **at no additional cost** during the warranty period.

Optional Maintenance Retainer (Proposed after Warranty): For Year 2, we offer a simple 10% of project fee annual retainer for security updates, plugin maintenance, and 10 hours of content changes.

20.2 Support Services

Following system go-live and during the warranty period, eTech S.C. shall provide structured application and technical support services.

Support Scope Includes:

- Application support for functional issues
- Technical support for system availability and integrations
- Assistance with configuration issues
- Issue analysis, resolution, and escalation

Support services shall be provided through agreed communication channels and response procedures.

Support Response Time Matrix

Severity Level	Description	Initial Response Time	Resolution Target
Critical (Severity 1)	Complete system outage, major service unavailability, or critical issue impacting core insurance operations (e.g., policy issuance, claims processing, payments)	≤ 2 hours	≤ 8 hours
High (Severity 2)	Significant functionality impairment with no immediate workaround; major impact on operations but system partially functional	≤ 4 hours	≤ 24 hours
Medium (Severity 3)	Functional issues with workaround available; limited operational impact	≤ 1 business day	≤ 3 business days
Low (Severity 4)	Minor issues, cosmetic defects, or general inquiries with no operational impact	≤ 2 business days	As scheduled / Next release

20.3 Post-Warranty Maintenance and Support


Upon completion of the warranty period, eTech S.C. shall offer **Annual Maintenance and Support (AMS)** services under mutually agreed terms.





Post-warranty support may include:

- Continued application and technical support
- System updates and patches
- Performance monitoring and optimization
- Support for future enhancements as required

Commercial details for AMS shall be provided separately in the financial proposal, as required by the RFP.

21. Mockups

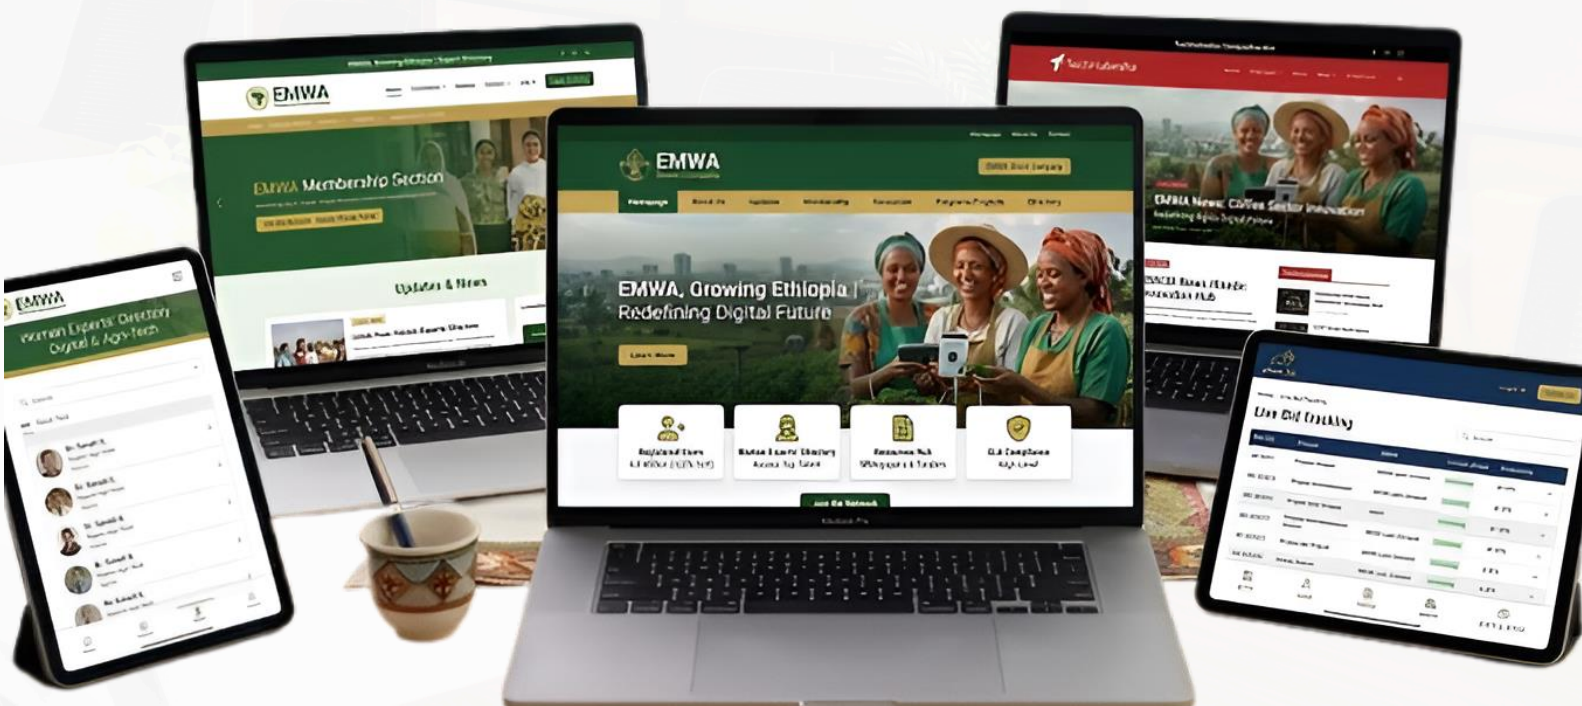



22. Relevant Experience

(Completed Website Projects)


22.1 Overview

eTech S.C. has successfully designed, developed, and deployed a wide range of institutional and corporate websites across multiple sectors in Ethiopia. These projects demonstrate our proven ability to deliver secure, scalable, and high-performing digital platforms tailored to organizational needs.


22.2 Some Key Completed Projects

The following are selected websites delivered by eTech S.C.:


1. Zemen Insurance

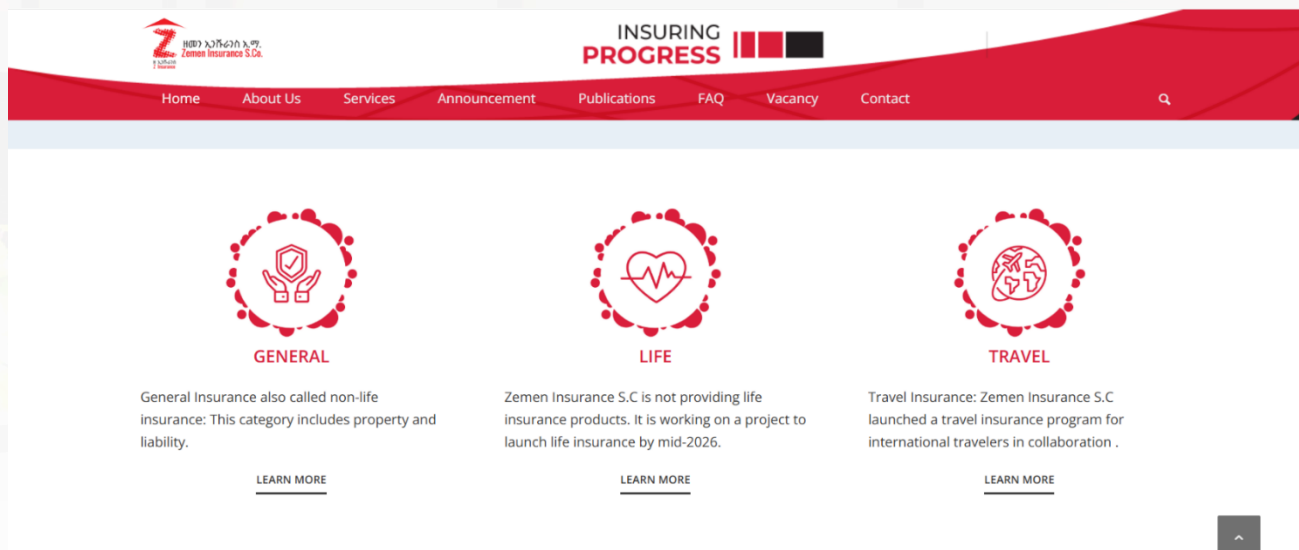

2. Addis International Convention Center (AICC)

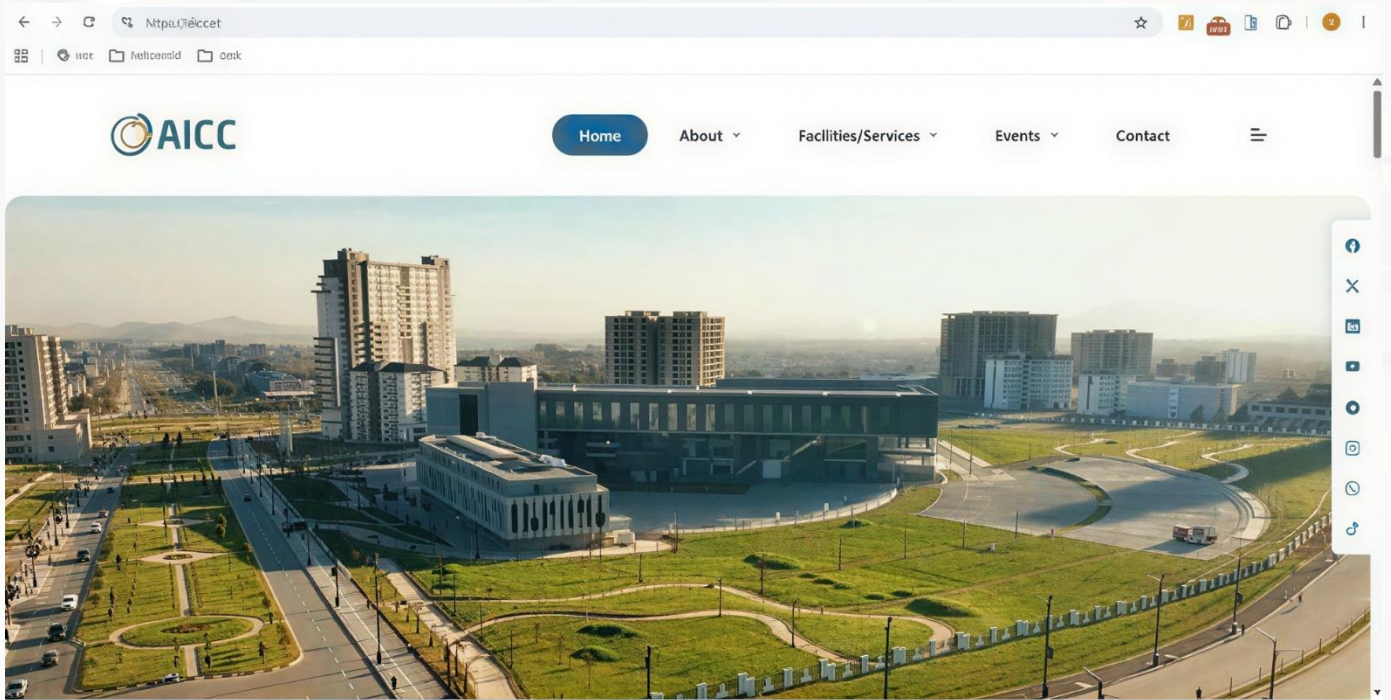


3. Awach Insurance

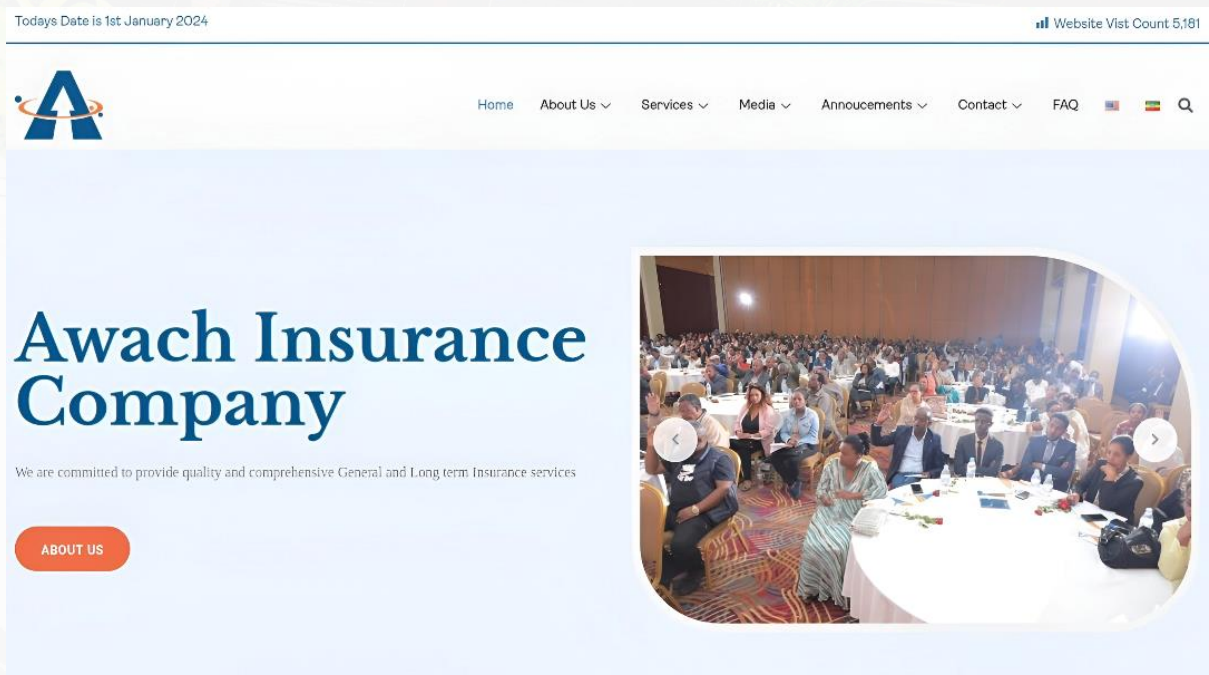


4. Addis Cardiac Center




5. Sheger SACCO



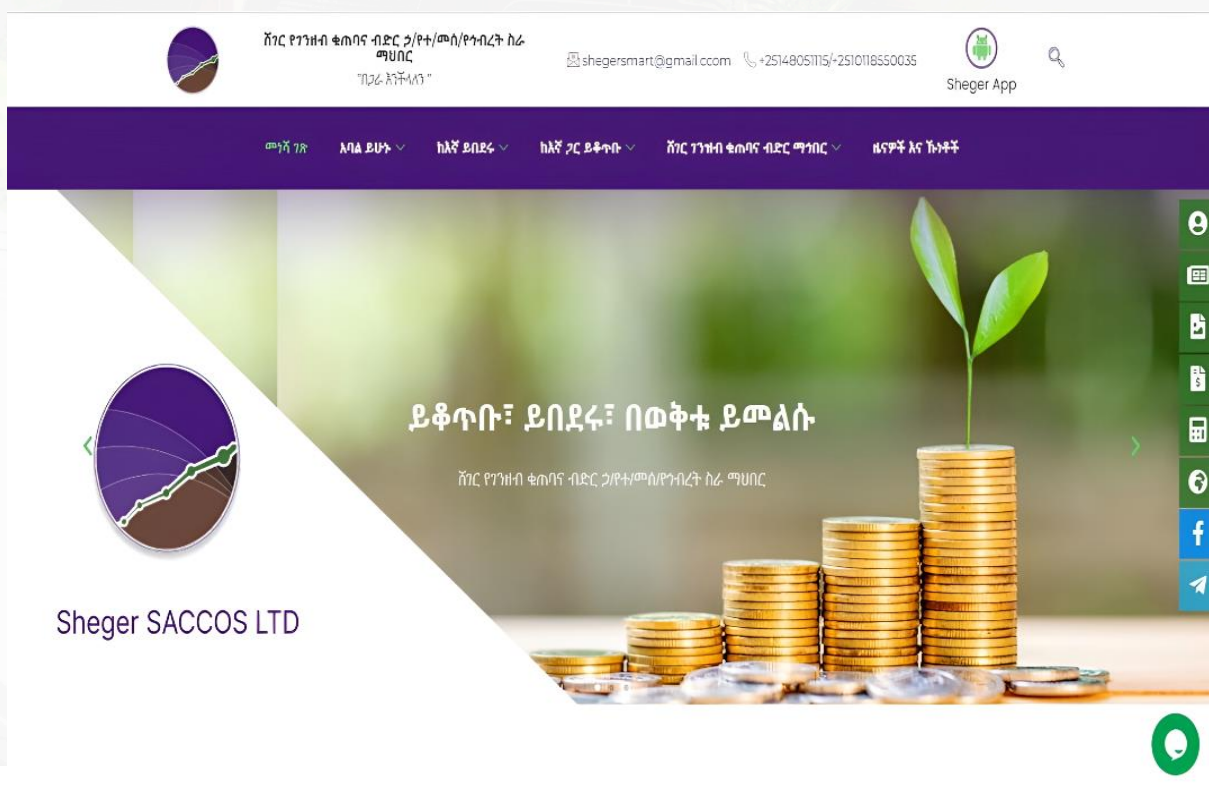


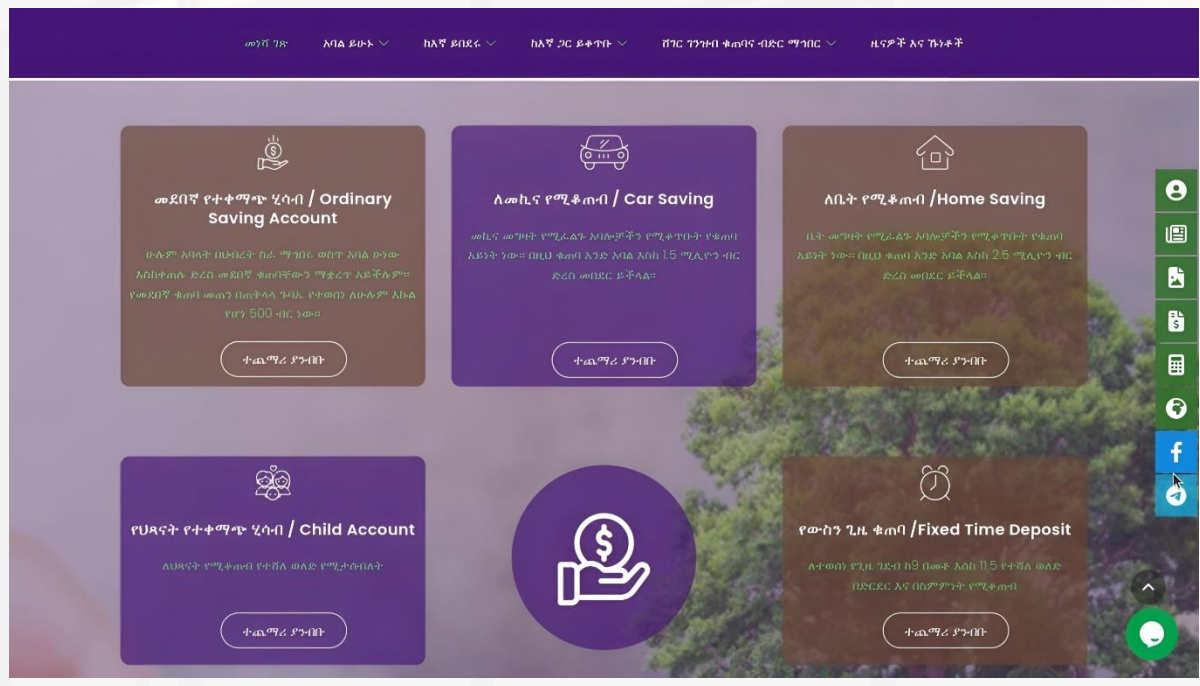

6. www.meqrezhealth.com

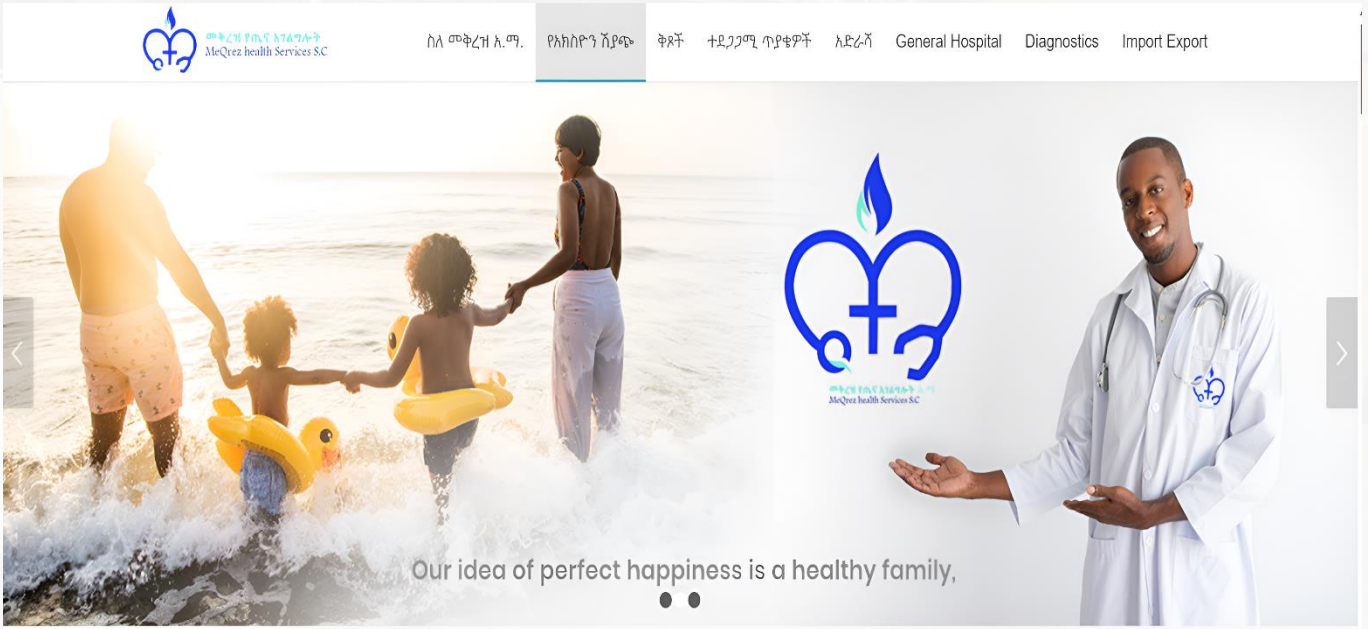

7. eTech SC.

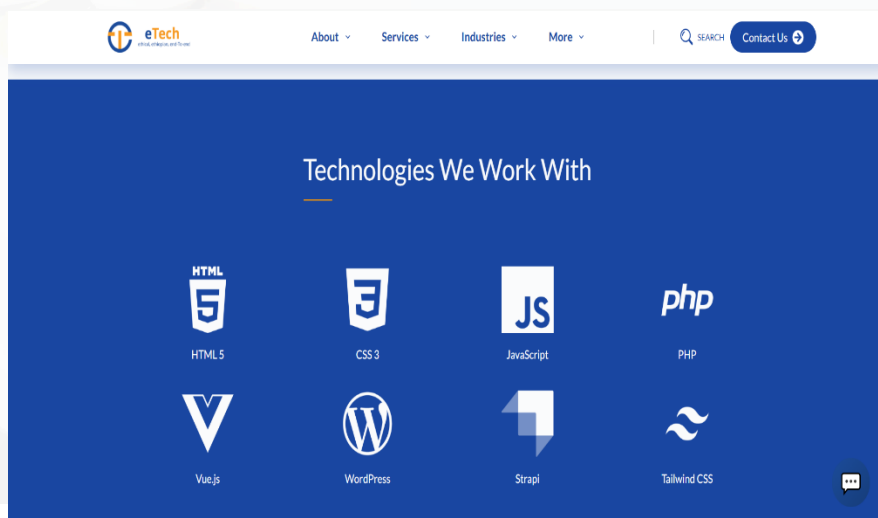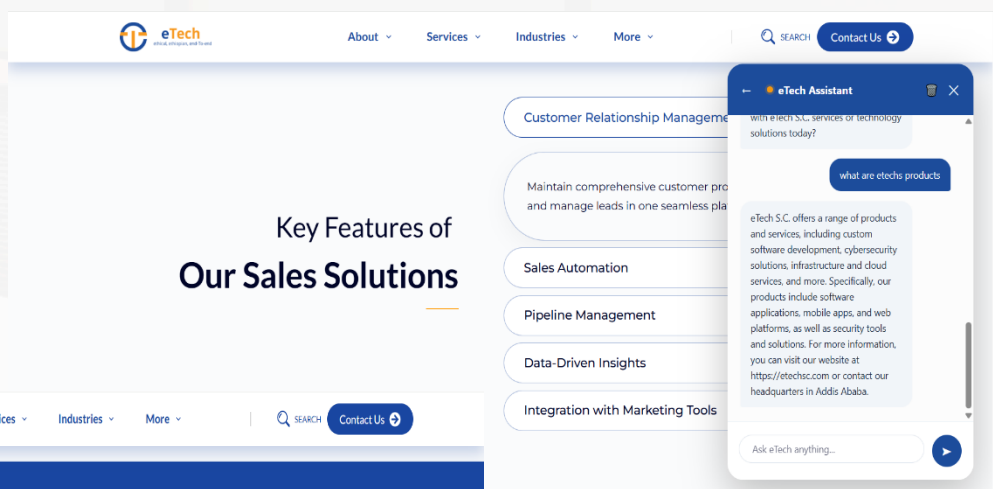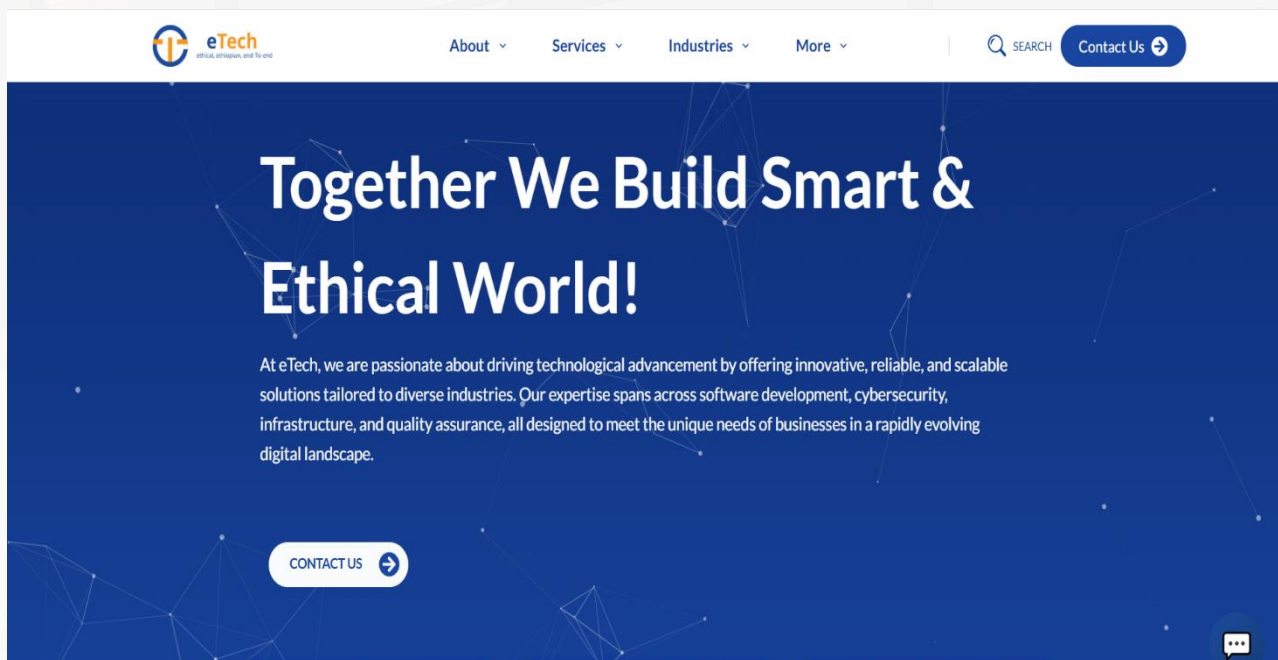

23. Source Code Handover

Upon successful completion of the project and formal acceptance by the Ethiopian Media Women Association (EMWA), eTech S.C. shall hand over the relevant source code for all software components developed or customized specifically for this project.

The source code will be provided in accordance with the terms of the contract and applicable Non-Disclosure Agreement (NDA), and will be shared solely for the purposes of operating, maintaining, and further enhancing the implemented website platform.

This handover applies exclusively to the deliverables developed under this project. All source code and related technical materials will be treated as confidential and subject to the agreed confidentiality and data protection provisions.

24. Declarations, Confirmations & NDA

Acknowledgement

24.1 Declaration

eTech S.C. hereby declares that all information provided in this proposal is accurate, complete, and submitted in good faith. We confirm that the proposed solution fully aligns with the requirements outlined in the EMWA Terms of Reference and that all services will be delivered in accordance with the agreed scope, timeline, and quality standards.

24.2 Compliance Confirmation

eTech S.C. confirms its full compliance with all applicable legal, technical, and operational requirements related to this project.

We further confirm that:

- The proposed solution adheres to relevant industry standards and best practices
- All implementation activities will be conducted in a professional and ethical manner
- The project will be delivered in accordance with agreed contractual obligations

24.3 Confidentiality & NDA Acknowledgement

eTech S.C. acknowledges the confidential nature of all information shared by EMWA during the course of this engagement.

We commit to:

- Treat all project-related information as confidential
- Use such information solely for the purpose of project implementation
- Not disclose any sensitive information to third parties without prior written consent from EMWA

eTech S.C. agrees to comply with any Non-Disclosure Agreement (NDA) or confidentiality requirements specified by EMWA as part of this project.

24.4 Non-Disclosure Commitment

All data, documents, and information obtained during the project will be securely handled and protected against unauthorized access, disclosure, or misuse.

Appropriate technical and organizational measures will be implemented to ensure data confidentiality and integrity throughout the project lifecycle.

24.5 Authorization

This proposal is submitted by eTech S.C. with full authority to undertake the responsibilities outlined herein.

Authorized representative details:

Name of Authorized Signatory: _____

Title: _____ Deputy CEO

Company: _____ eTech S.C.

Signature: _____

Date: _____ 22/05/2026





